

RAILROAD COMMISSION OF TEXAS

CHRISTI CRADDICK, *CHAIRMAN*
RYAN SITTON, *COMMISSIONER*
WAYNE CHRISTIAN, *COMMISSIONER*

INTERNAL
OIL AND GAS DIVISION
SANTOS GONZALES JR., P.E.,
ASSISTANT DIRECTOR, FIELD OPERATIONS

MEMORANDUM

June 11, 2017

MEMORANDUM TO: Chairman Christi Craddick
Commissioner Ryan Sitton
Commissioner Wayne Christian


FROM: Santos Gonzales, Jr., P.E.
Assistant Director, Field Operations

SUBJECT: Field Operations Section
Monthly Report of State-funded Well Plugging Activities
June 2017, FY 2017

Attached is the monthly report titled "State-funded Well Plugging Activities" for the Field Operations Section of the Oil and Gas Division. This report contains the following:

1. Monthly and cumulative performance measure summaries of the state-funded well plugging activities of this Section.
2. Summary graphs of wells plugged, cost of wells plugged, number of salvage operations, and salvage proceeds.
3. A list of state-funded plugging contracts in excess of \$100,000 where the original encumbered amount has been exceeded by 10% or more. The contracts will be carried on this report until completed.

SG:th
Attachments


Santos Gonzales, Jr., P.E.
Assistant Director, Oil & Gas Division

cc: Kimberly Corley, Executive Director
Wei Wang, Chief Financial Officer
Lori Wrotenbery, Director, Oil & Gas Division
David Cooney, Director, Office of General Counsel-Enforcement
Paul Delaney, Internal Auditor
Stacie Fowler, Director, Governmental Affairs
Ramona Nye, Media Affairs
Tina Beck, Analyst, Legislative Budget Board
Craig Bean, Policy Advisor, Office of the Governor
District Directors (via email)

RAILROAD COMMISSION OF TEXAS
Oil and Gas Division
Field Operations Section
Monthly State-Funded Plugging Activities
June 2017

Outcome Measure: Percentage of Known Orphaned Wells Plugged with the Use of State Funds (State-Funded Plugging/Orphaned Wells).

June	1.54%
Fiscal Year-to-date	6.85%
Performance Measure Goal	6 %

Output Measure: Number of Orphaned Wells Plugged with the Use of State Funds.

June	134
Fiscal Year-to-date	595
Performance Measure Goal	875

Output Measure: Total Aggregate Plugging Depth of Wells Plugged with the Use of State Funds.

June	318,583
Fiscal Year-to-date	1,192,074
Performance Measure Goal	1,671,250

Efficiency Measure: Average Number of Days to complete a State-Funded Well Plugging.

	From Contract Award Date
June	28
Fiscal Year-to-date	43
Performance Measure Goal	75

Explanatory Measure: Number of Orphaned Wells Approved for Plugging with the Use of State Funds.

June	119
Fiscal Year-to-date	892
Performance Measure Goal	800

Explanatory Measure: Number of Known Orphaned Wells in Non-compliance with the Commission's Plugging Rule.

	Orphaned wells
June	8,680
Performance Measure Goal	9,000

Explanatory Measure: Number of Wells Plugged, by Operators, Without the Use of State Funds.

June	791
Fiscal Year-to-date	9,445
Performance Measure Goal	5,200

Explanatory measure: Percentage of Active Well Operators Who Have More Than 25% of Their Wells Inactive.

June	41%
Performance Measure Goal	42%

Explanatory measure: Numbered shut-in/inactive wells.

June	117,574
Performance Measure Goal	110,000

RAILROAD COMMISSION OF TEXAS
Oil Field Cleanup

Monthly State-Funded Plugging, Pollution Abatement and Salvage Activities
Commissioners Report
06/01/2017 to 06/30/2017

State-Funded Plugging Activities

Number of wells approved for plugging this month	119
Estimated cost of approvals	\$ 1,625,760.00
Number of wells approved for this fiscal year	892
Number of approved wells remaining to plug	1397
Estimated cost to plug remaining approvals	\$ 32,114,761.09
Number of pluggings completed this month	134
Total cost to plug wells completed this month	\$ 2,235,676.83
Number of pluggings completed this fiscal year	595
Cost of pluggings completed this fiscal year	\$ 7,625,960.96


Pollution Abatement Activities

Number of pollution abatements approved this month	2
Estimated cost of approvals	\$ 35,000.00
Number of pollution abatements approved for this fiscal year	43
Number of pollution abatements remaining	57
Estimated cost to pollution abatements remaining	\$ 196,280.00
Number of pollution abatements completed this month	2
Total cost of pollution abatements completed this month	\$ 10,018.75
Number of pollution abatements completed this fiscal year	28
Cost of pollution abatements completed this fiscal year	\$ 348,380.79

Salvage Activities


Number of salvage activities completed this month	27
Total proceeds received this month	\$ 37,929.50
Number of salvage activities completed this fiscal year	97
Total proceeds received this year	\$ 156,603.33

State-funded Well Plugging Program Monthly Wells Plugged June 2017

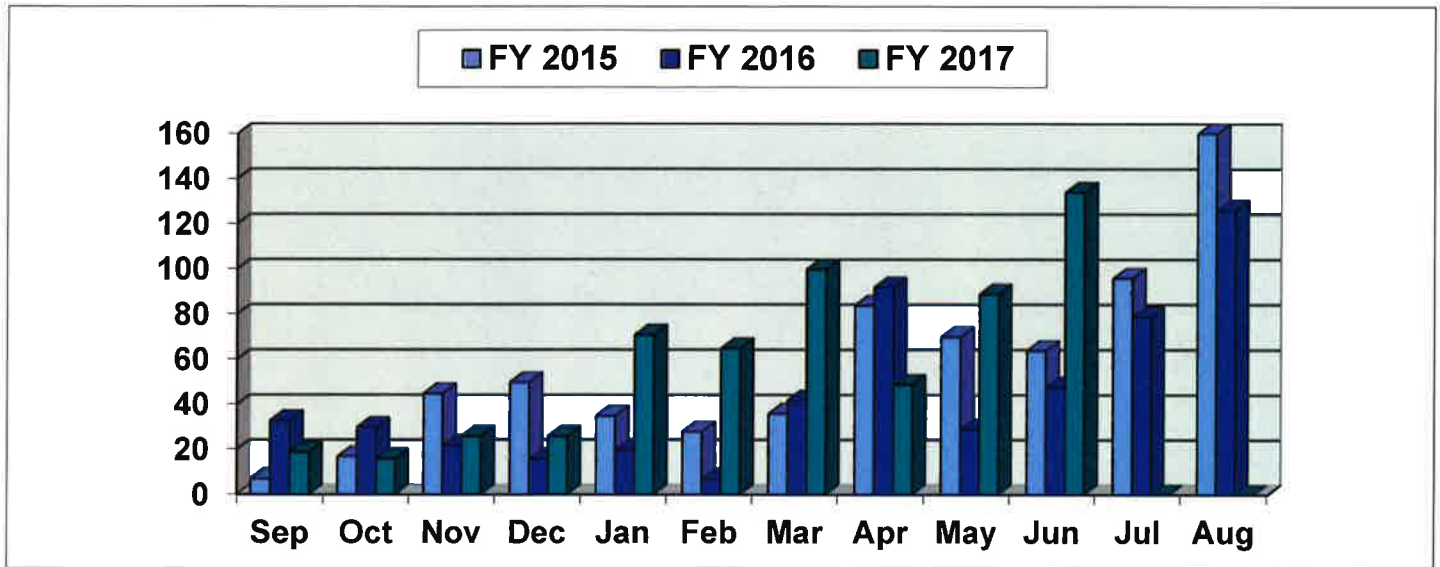


	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Tot
FY 2015	7	17	45	50	35	28	36	84	70	64	96	160	692
FY 2016	33	30	22	16	20	7	42	92	29	48	79	126	544
FY 2017	19	16	26	26	71	65	100	49	89	134	0	0	595

State-funded Well Plugging Program Monthly Cost of Wells Plugged June 2017

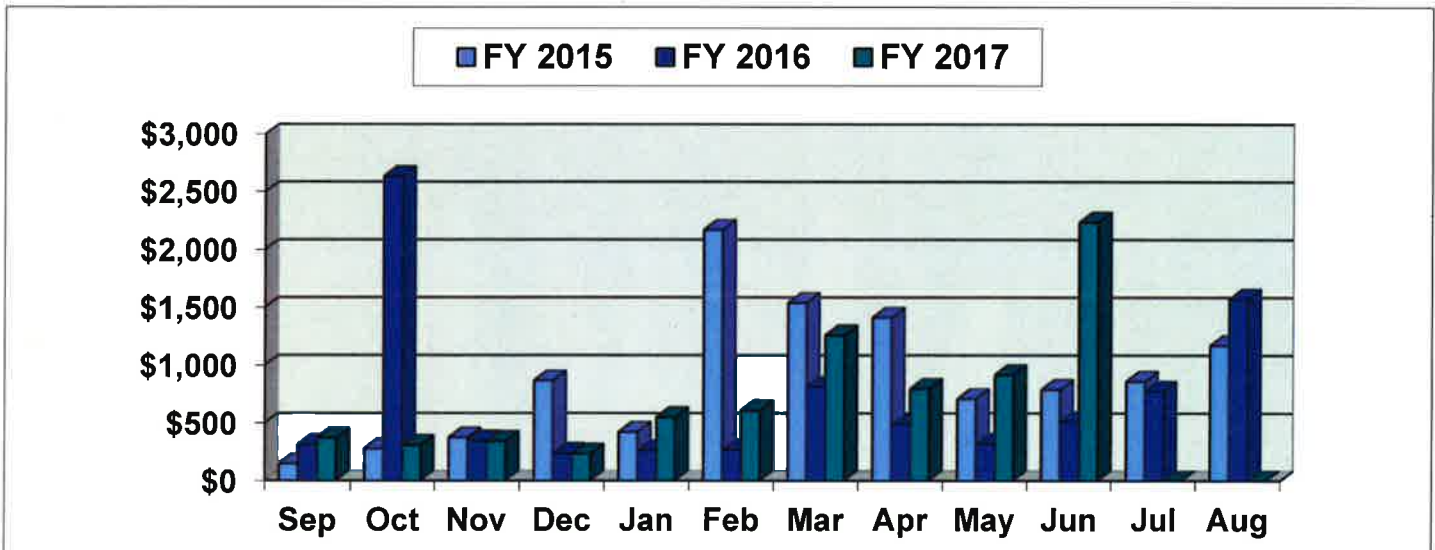


\$M	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Tot
FY 2015	\$146	\$277	\$374	\$866	\$422	\$2,169	\$1,538	\$1,411	\$709	\$789	\$860	\$1,170	\$10,731
FY 2016	\$314	\$2,633	\$348	\$240	\$264	\$266	\$814	\$488	\$322	\$511	\$775	\$1,571	\$8,546
FY 2017	\$372	\$308	\$344	\$235	\$550	\$609	\$1,260	\$796	\$916	\$2,236	\$0	\$0	\$7,626

State-funded Well Plugging Program Cumulative Wells Plugged June 2017

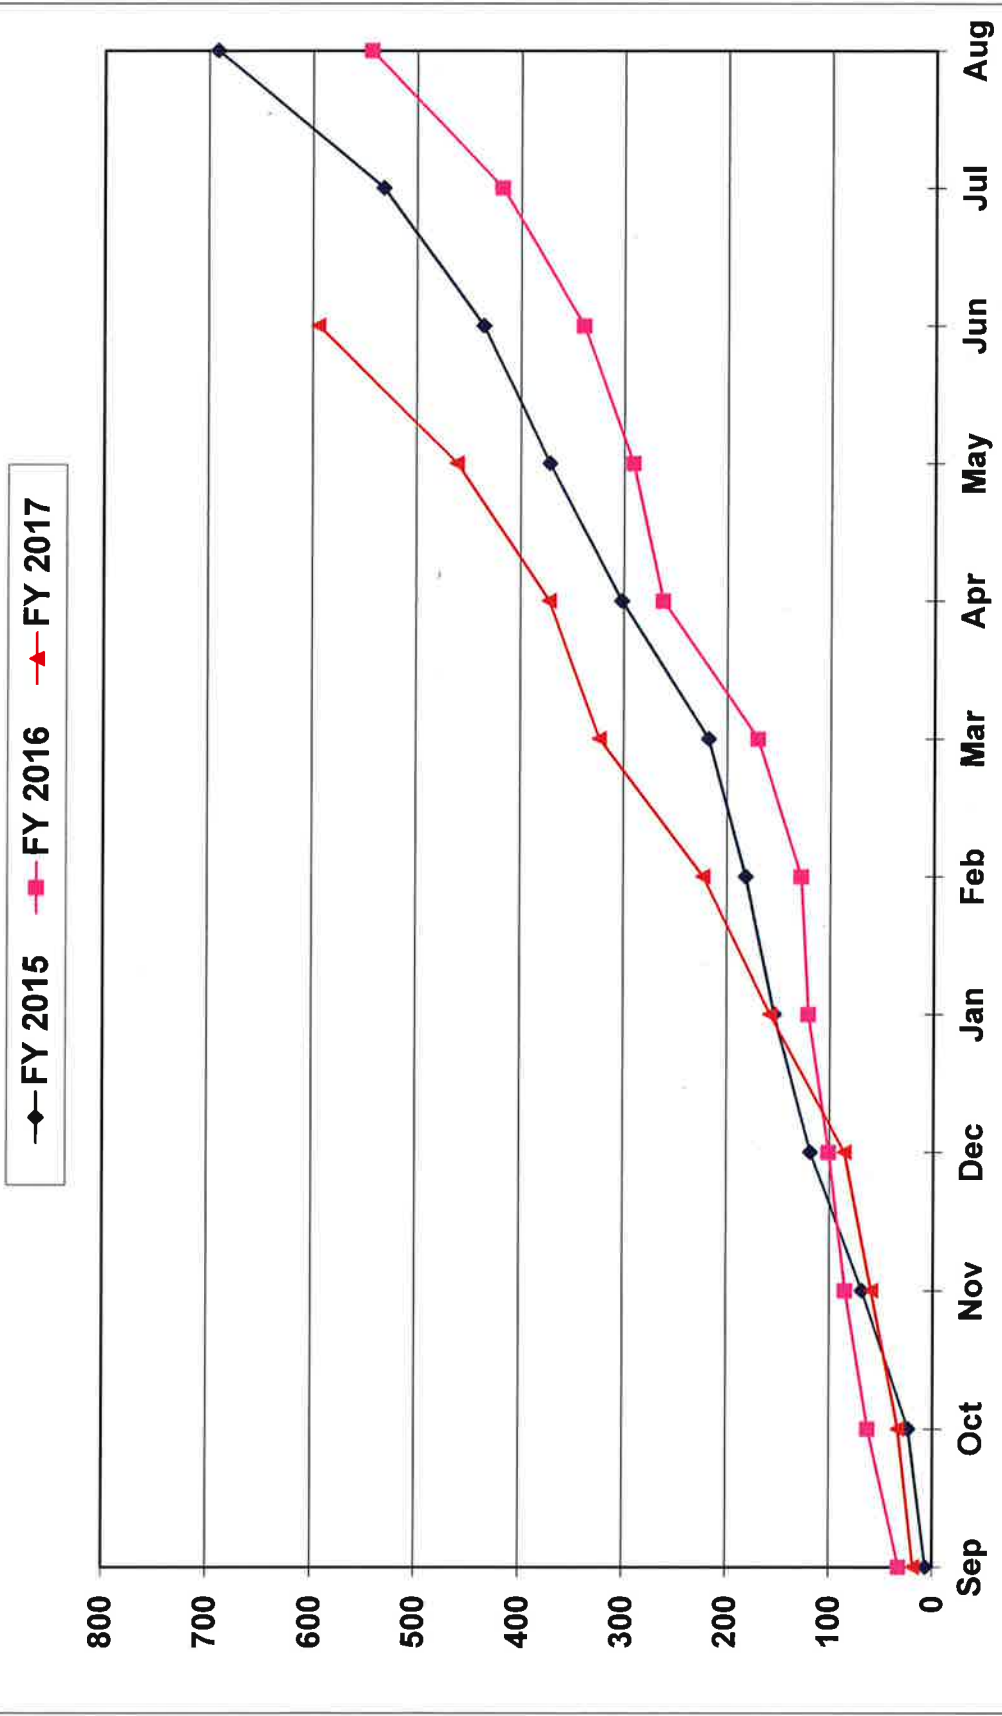


State-funded Well Plugging Program Monthly Salvage Operations June 2017

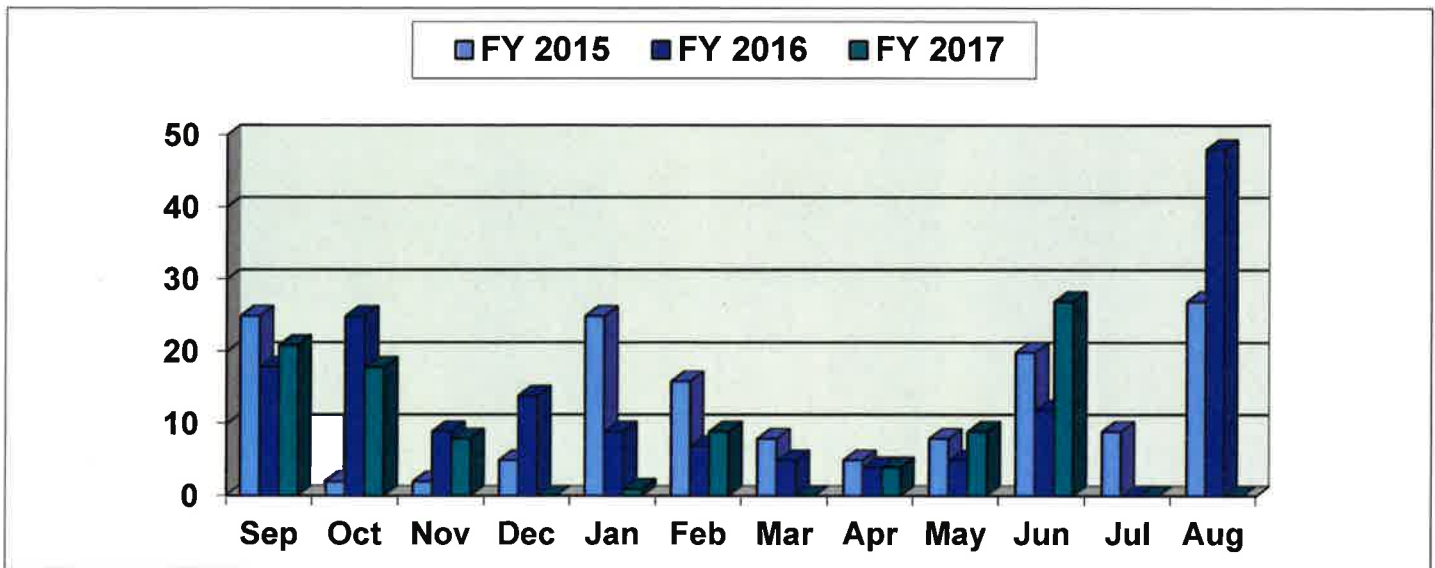


	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Tot
FY 2015	25	2	2	5	25	16	8	5	8	20	9	27	152
FY 2016	18	25	9	14	9	7	5	4	5	12	0	48	156
FY 2017	21	18	8	0	1	9	0	4	9	27	0	0	97

State-funded Well Plugging Program Monthly Salvage Proceeds June 2017

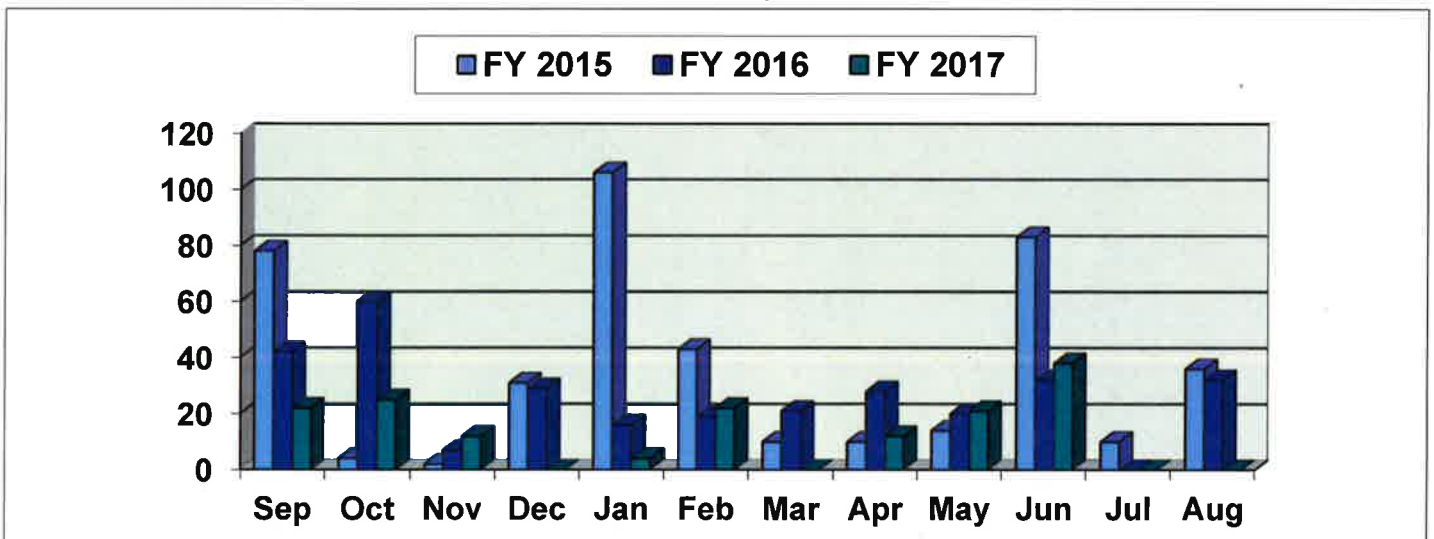

\$M	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Tot
FY 2015	\$78	\$4	\$2	\$31	\$106	\$43	\$10	\$10	\$14	\$83	\$10	\$36	\$427
FY 2016	\$42	\$60	\$7	\$29	\$16	\$19	\$21	\$28	\$20	\$32	\$0	\$32	\$306
FY 2017	\$22	\$25	\$12	\$0	\$4	\$22	\$0	\$12	\$21	\$38	\$0	\$0	\$156

State-funded Well Plugging Program Cumulative Salvage Proceeds June 2017

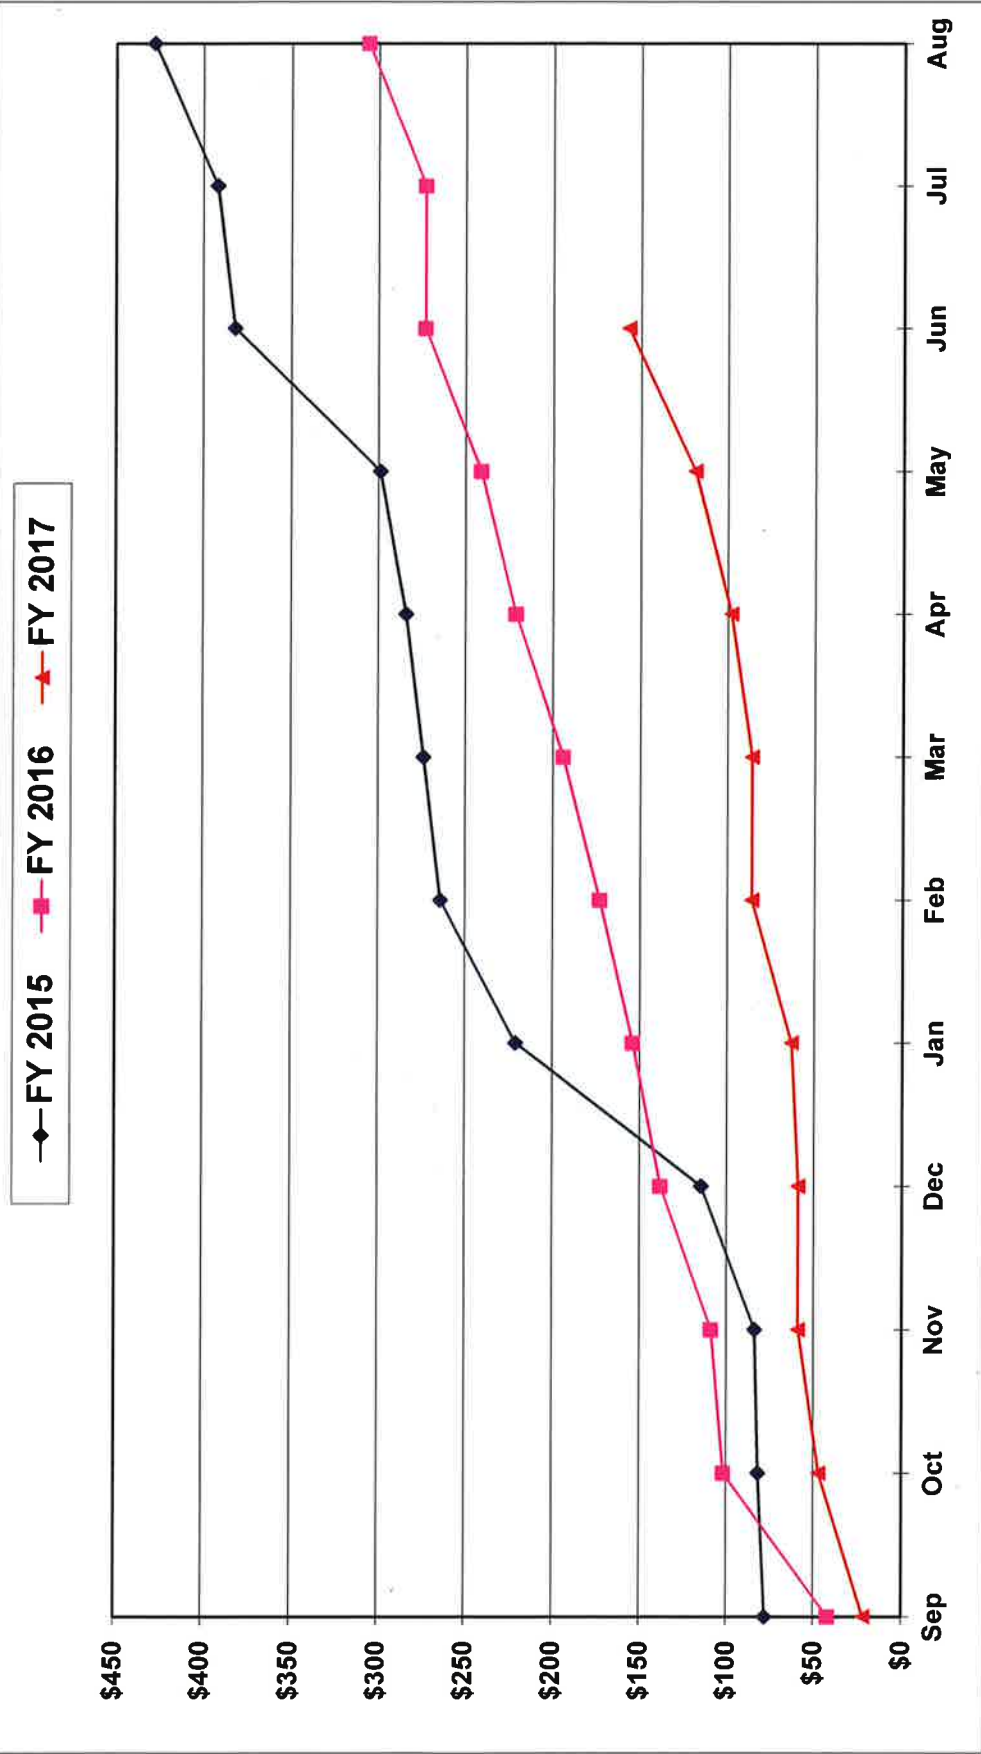

\$M	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
FY 2015	\$78	\$82	\$84	\$115	\$221	\$264	\$274	\$284	\$299	\$382	\$392	\$428
FY 2016	\$42	\$102	\$109	\$138	\$154	\$173	\$194	\$221	\$241	\$273	\$273	\$306
FY 2017	\$22	\$47	\$59	\$59	\$63	\$86	\$86	\$98	\$119	\$157		

RAILROAD COMMISSION OF TEXAS
Oil Field Cleanup
Fiscal Year State-funded Plugging Summary
06/30/2017

Run Date: July 11, 2017

Fiscal Year	Pluggings Approved	Pluggings Completed	Plugging Cost
1984	421	177	\$ 1,112,197.81
1985	474	392	\$ 2,028,121.62
1986	533	714	\$ 2,583,271.00
1987	709	703	\$ 2,106,546.67
1988	830	627	\$ 2,162,255.30
1989	844	578	\$ 2,028,764.38
1990	1004	432	\$ 1,993,128.18
1991	667	455	\$ 2,157,121.78
1992	2412	1324	\$ 5,692,878.50
1993	1171	1404	\$ 6,680,547.97
1994	1106	1325	\$ 6,003,267.26
1995	1381	1364	\$ 6,110,031.51
1996	1286	1366	\$ 5,259,382.52
1997	2156	1577	\$ 7,077,979.66
1998	1854	1604	\$ 8,456,131.53
1999	1318	1126	\$ 4,481,066.50
2000	1693	1335	\$ 5,134,842.14
2001	1612	1417	\$ 6,686,357.01
2002	1659	1464	\$ 8,011,659.30
2003	1469	1635	\$ 7,211,207.33
2004	1701	1525	\$ 7,398,237.94
2005	2168	1710	\$ 11,360,931.62
2006	1815	1824	\$ 10,736,521.32
2007	1707	1536	\$ 18,537,524.65
2008	1826	1261	\$ 14,737,537.15
2009	1557	1460	\$ 16,700,337.18
2010	1216	1182	\$ 10,504,966.23
2011	974	802	\$ 9,233,659.43
2012	761	766	\$ 12,427,517.08
2013	840	780	\$ 21,024,684.98
2014	626	564	\$ 15,069,502.11
2015	736	692	\$ 10,731,174.12
2016	811	544	\$ 8,546,936.52
2017	893	595	\$ 7,625,960.96
Totals	42230	36260	\$ 267,612,249.26

RAILROAD COMMISSION OF TEXAS
Oil Field Cleanup
Fiscal Year Summary for Pollution Abatements
06/30/2017

Run Date: July 11, 2017

Fiscal Year	PAs Approved	PAs Completed	PAs Cost
1984			
1985	21	14	\$ 3,563.32
1986	22	25	\$ 34,817.01
1987	42	31	\$ 25,702.15
1988	46	37	\$ 17,519.39
1989	95	72	\$ 23,521.25
1990	78	65	\$ 28,222.43
1991	146	124	\$ 72,631.81
1992	129	127	\$ 71,268.54
1993	160	124	\$ 46,586.49
1994	97	84	\$ 43,771.43
1995	86	68	\$ 29,567.34
1996	124	100	\$ 47,895.29
1997	137	73	\$ 38,268.97
1998	174	148	\$ 92,235.78
1999	136	157	\$ 70,854.70
2000	151	79	\$ 359,441.08
2001	115	61	\$ 116,091.54
2002	125	85	\$ 146,095.87
2003	117	223	\$ 161,975.21
2004	125	170	\$ 135,450.45
2005	93	121	\$ 415,879.04
2006	135	75	\$ 72,209.86
2007	83	54	\$ 546,481.92
2008	140	123	\$ 224,762.50
2009	92	58	\$ 147,553.92
2010	103	167	\$ 234,020.62
2011	62	59	\$ 119,330.15
2012	54	43	\$ 456,770.84
2013	56	57	\$ 407,575.65
2014	47	42	\$ 150,412.10
2015	54	82	\$ 227,302.24
2016	43	39	\$ 82,313.69
2017	41	29	\$ 348,380.79
Totals	3129	2816	\$ 4,998,473.37

Oil and Gas Division
 Field Operations Section
 State-Funded Plugging
 Contracts Exceeding \$100,000
 Original Encumbered Amount Exceeded by 10% or More
 June 2017, FY 17

District	Requisition #	Contractor	Original Encumbrance	Current Encumbrance	\$ Increase	% Increase	Remarks
1/2	455-16-0908	Newman Operating Company	\$112,340.00	\$360,340.00	\$40,000.00	220.76%	Increase contract value to, downhole problems encountered.
	455-16-1035	Newman Operating Company	\$158,975.00	\$178,975.00	\$20,000.00	12.58%	Increase contract value to, downhole problems encountered.
3	455-16-0163	Delta Seaboard	\$228,522.00	\$456,522.00	\$228,000.00	99.77%	Add ten (10) wells to existing contract.
					\$0.00		
4	455-16-1004	Newman Operating Company	\$200,885.00	\$644,000.00	\$100,000.00	220.58%	Increase contract value to, downhole problems encountered.
5/6	455-16-0906	Topcat Well Service	\$108,896.00	\$528,096.00	\$50,000.00	384.95%	Add one (1) well to existing contract.
	455-16-0050	Topcat Well Service	\$198,398.00	\$368,398.00	\$10,000.00	85.69%	Increase contract value to, downhole problems encountered.
7B	455-16-0903	Mash Oilfield Services	\$84,320.00	\$176,320.00	\$92,000.00	109.11%	Adding eight (8) wells to the existing contract.
	455-16-8010	2W Petroleum	\$30,000.00	\$110,000.00	\$110,000.00	266.67%	Emergency Well Plug in Dist 7B
	455-16-1028	Hay Creek Investments	\$99,310.00	\$154,310.00	\$55,000.00	55.38%	Adding eleven (11) wells to existing contract.
7C	455-16-0771	Quail Well Service, Inc.	\$216,620.00	\$287,620.00	\$71,000.00	32.78%	Add four (4) wells to contract.
8/A	455-17-8016	Etech Environmental & Safety	\$30,000.00	\$780,000.00	\$780,000.00	2500.00%	Emergency Well Plug in Dist 08
	455-17-8019	TODPAT 6	\$40,000.00	\$690,000.00	\$690,000.00	1625.00%	Emergency Well Plug in Dist 08
	455-17-8042	TODPAT 6	\$50,000.00	\$150,000.00	\$100,000.00	200.00%	Emergency Well Plug in Dist 08
9	455-17-0289	SPH Development	\$71,225.00	\$347,925.00	\$119,700.00	388.49%	Add thirty-three wells to existing contract.
	455-16-0911	Moore Energy	\$125,062.00	\$507,762.00	\$112,700.00	306.01%	Add Twenty-one (21) to existing contract.
10	455-						
