RAILROAD COMMISSION OF TEXAS

WAYNE CHRISTIAN, CHAIRMAN CHRISTI CRADDICK, COMMISSIONER RYAN SITTON, COMMISSIONER

INTERNAL
OIL AND GAS DIVISION
CLAY WOODUL
ASSISTANT DIRECTOR, FIELD OPERATIONS

MEMORANDUM

July 8, 2019

MEMORANDUM TO:

Chairman Wayne Christian Commissioner Christi Craddick Commissioner Ryan Sitton

FROM:

Clay Woodul

Assistant Director, Oil and Gas Division

Field Operations

SUBJECT:

Field Operations Section

Monthly Report of State Managed Well Plugging Activities

June 2019, FY 2019

Attached is the monthly report titled "State Managed Well Plugging Activities" for the Field Operations Section of the Oil and Gas Division. This report contains the following:

- 1. Monthly and cumulative performance measure summaries of the state managed well plugging activities of this Section.
- 2. Summary graphs of wells plugged, cost of wells plugged, number of salvage operations, and salvage proceeds.

The information contained in this report includes only those wells that have been physically plugged, invoiced by the plugging contractor, and approved for payment by Field Operations. Plugging operations are tracked daily to monitor the progress in meeting the FY 2019 goal of plugging 1,560 wells. As of June 30, 2019, a total of 1,440 wells have been physically plugged, though not all of them have yet been invoiced and approved for payment.

KCW Attachments Clay Woodul

Assistant Director, Oil and Gas Division

Field Operations

cc:

Wei Wang, Executive Director

Danny Sorrells, Director, Oil & Gas Division

Megan Neal, Director, Office of General Counsel-Enforcement

Jeremy Mazur, Director Government Relations

Paul Delaney, Internal Auditor

Ramona Nye, Media Affairs

Thomas Brown, Analyst, Legislative Budget Board Stacie Bennett, Policy Advisor, Office of the Governor

District Directors (via email)

RAILROAD COMMISSION OF TEXAS

Oil and Gas Division

Field Operations Section Monthly State Managed Plugging Activities

June 2019

Outcome Measure: Percentage of Known Orphaned Wells Plugged with the Use of State Funds (State Managed Plugging/Orphaned Wells).

June2.22%Fiscal Year-to-date20.44%Performance Measure Goal14.5 %

Output Measure: Number of Orphaned Wells Plugged with the Use of State Funds.

June140Fiscal Year-to-date1,289Performance Measure Goal979

Output Measure: Total Aggregate Plugging Depth of Wells Plugged with the Use of State Funds.

June 338,886
Fiscal Year-to-date 3,212,284
Performance Measure Goal 1,920,000

Efficiency Measure: Average Number of Days to complete a State Managed Well Plugging. From Contract Award Date

June 51 Fiscal Year-to-date 46 Performance Measure Goal 75

Explanatory Measure: Number of Orphaned Wells Approved for Plugging with the Use of State Funds.

June 130 Fiscal Year-to-date 1,414 Performance Measure Goal 1,000

Explanatory Measure: Number of Known Orphaned Wells in Non-compliance with the Commission's Plugging Rule.

June 6,306 Performance Measure Goal 8,800

Explanatory Measure: Number of Wells Plugged, by Operators, Without the Use of State Funds.

June193Fiscal Year-to-date3,743Performance Measure Goal6,200

Explanatory measure: Percentage of Active Well Operators Who Have More Than 25% of Their Wells Inactive.

June 43% Performance Measure Goal 40%

Explanatory measure: Numbered shut-in/inactive wells.

June 127,247 Performance Measure Goal 110,000


RAILROAD COMMISSION OF TEXAS Oil Field Cleanup

Monthly State-Funded Plugging, Pollution Abatement and Salvage Activities Commissioners Report

06/01/2019 to 06/30/2019


State-Funded Plugging Activities	
Number of wells approved for plugging this month	130
Estimated cost of approvals	\$ 4,210,850.00
Number of wells approved for this fiscal year	1414
Number of approved wells remaining to plug	1907
Estimated cost to plug remaining approvals	\$ 67,302,872.84
Number of pluggings completed this month	140
Total cost to plug wells completed this month	\$ 3,617,876.36
Number of pluggings completed this fiscal year	1289
Cost of pluggings completed this fiscal year	\$ 26,401,520.68
Pollution Abatement Activities	
Number of pollution abatements approved this month	1
Estimated cost of approvals	\$ 5,000.00
Number of pollution abatements approved for this fiscal year	40
Number of pollution abatements remaining	45
Estimated cost to pollution abatements remaining	\$ 423,900.00
Number of pollution abatements completed this month	1
Total cost of pollution abatements completed this month	\$ 5,792.00
Number of pollution abatements completed this fiscal year	18
Cost of pollution abatements completed this fiscal year	\$ 75,179.09
Salvage Activities	
Number of salvage activities completed this month	10
Total proceeds received this month	\$ 52,150.24
Number of salvage activities completed this fiscal year	174
Total proceeds received this year	\$ 582,953.68

State Managed Well Plugging Program Monthly Wells Plugged June 2019

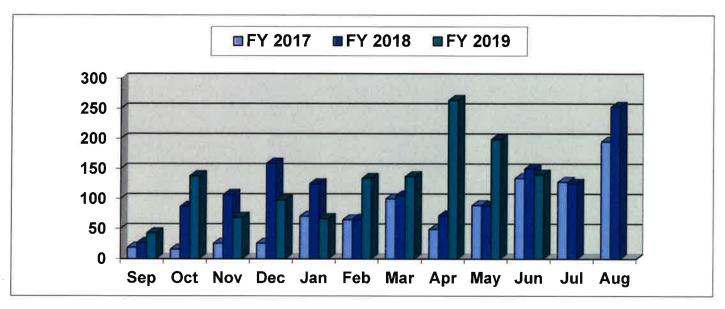


	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	Мау	Jun	Jul	Aug	Tot
FY 2017	19	16	26	26	71	65	100	49	89	134	128	195	918
FY 2018	27	87	107	159	125	66	105	72	88	150	125	253	1,364
FY 2019	43	138	69	98	67	134	137	264	199	140			1,289

State Managed Well Plugging Program Monthly Cost of Wells Plugged June 2019

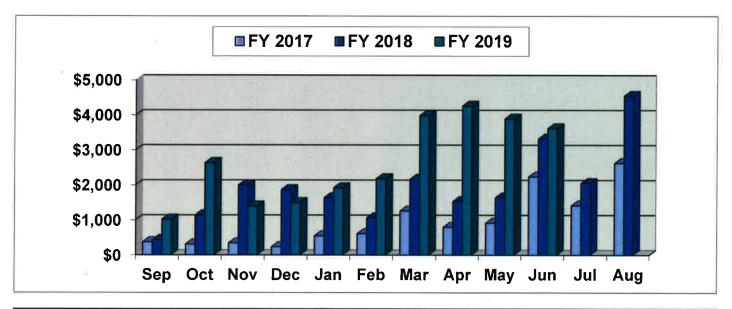

\$M	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Tot
FY 2017	\$372	\$308	\$344	\$235	\$550	\$609	\$1,260	\$796	\$916	\$2,236	\$1,412	\$2,626	\$11,664
FY 2018	\$433	\$1,144	\$1,996	\$1,865	\$1,636	\$1,064	\$2,163	\$1,532	\$1,639	\$3,319	\$2,052	\$4,550	\$23,393
FY 2019	\$1,020	\$2,637	\$1,397	\$1,494	\$1,921	\$2,181	\$3,983	\$4,257	\$3,894	\$3,617			\$26,401


State Managed Well Plugging Program Cumulative Wells Plugged June 2019

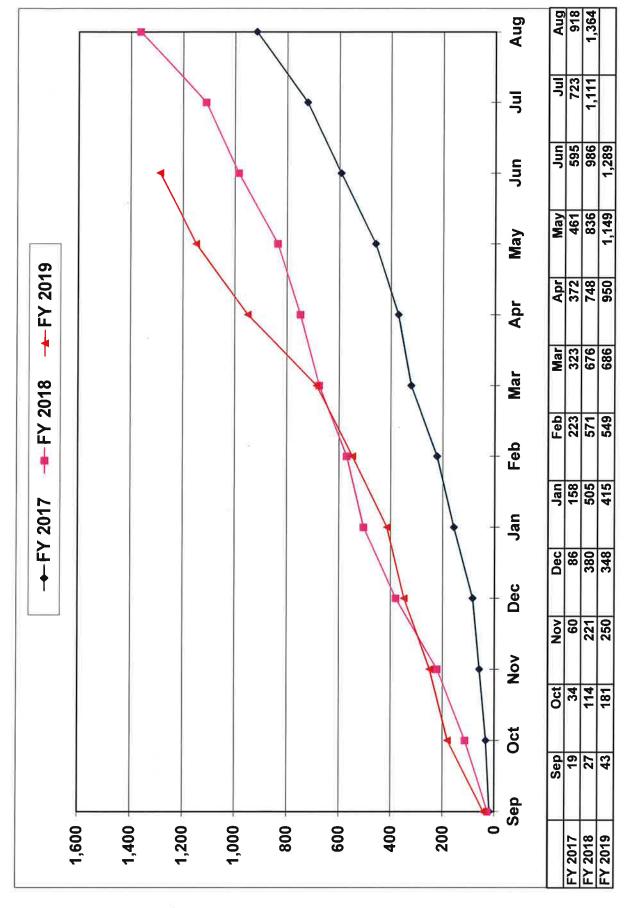

Page 4


State Managed Well Plugging Program **Monthly Salvage Operations**



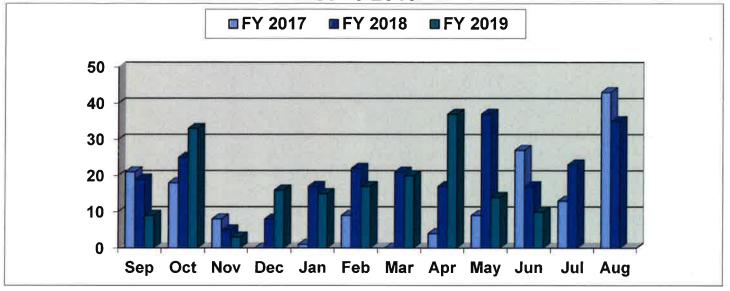


	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Tot
FY 2017	21	18	8	0	1	9	0	4	9	27	13	43	153
FY 2018	19	25	5	8	17	22	21	17	37	17	23	35	246
FY 2019	9	33	3	16	15	17	20	37	14	10			174

State Managed Well Plugging Program Monthly Salvage Proceeds June 2019

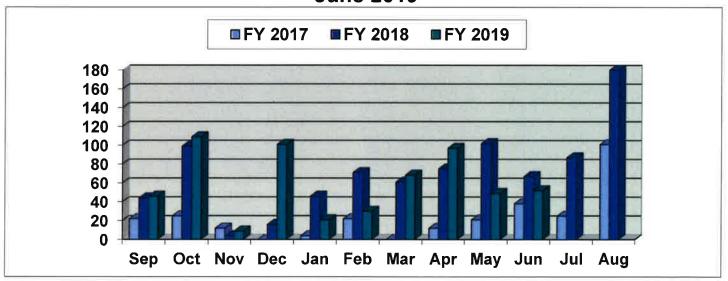

\$M	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Tot
FY 2017	\$22	\$25	\$12	\$0	\$4	\$22	\$0	\$12	\$21	\$38	\$25	\$101	\$282
FY 2018	\$44	\$99	\$4	\$16	\$46	\$71	\$61	\$75	\$102	\$67	\$87	\$180	\$852
FY 2019	\$46	\$109	\$9	\$101	\$21	\$30	\$68	\$97	\$49	\$52			\$583

State Managed Well Plugging Program Cumulative Salvage Proceeds June 2019

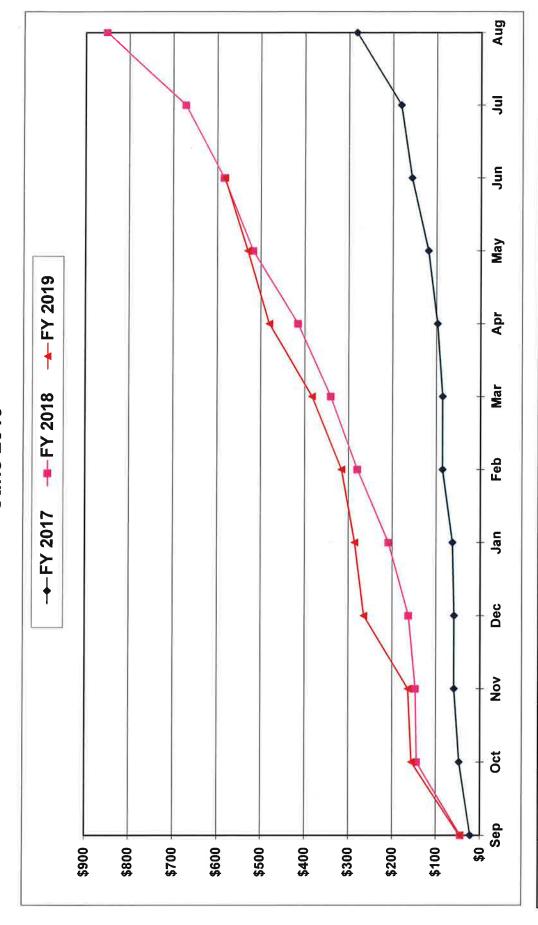

SM S	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
FY 2017	\$22	\$47	\$29	\$59	\$63	98\$	\$86	86\$	\$119	\$157	\$182	\$283
FY 2018	\$44	\$144	\$147	\$163	\$209	\$280	\$341	\$416	\$518	\$585	\$672	\$852
FY 2019	\$46	\$156	\$164	\$265	\$286	\$316	\$384	\$481	\$530	\$583		
						Page 6						
